

# PROGRES DLA POWŁOKI OGNIOOCHRONNEJ

PROGRESS FOR FIRE PROTECTION

Progres na dzień:

Progress for day:

**07.11.2021**

## TUNEL LEWY


TUNNEL LEFT

## POZOSTAŁO DO WYKONANIA

TO FINISH

		wg osi tunelu / by axis of the tunnel		wykonano / done	
<b>POWŁOKA OGNIOOCHRONNA</b> FIRE PROTECTION	start km	<b>721 818,46</b>		<b>104,31</b>	[mb] [lm]
	end km	<b>721 922,77</b>		5 [%]	

<b>POWŁOKA OGNIOOCHRONNA</b> FIRE PROTECTION	<b>1 955,15</b>	[mb] [lm]
---	-----------------	--------------

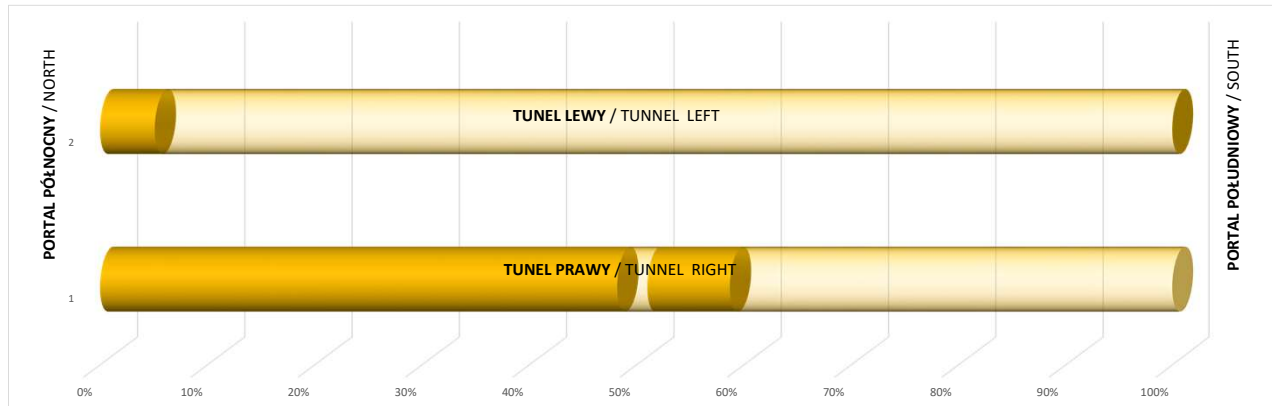

## TUNEL LEWY I PRAWY

TUNNEL LEFT AND RIGHT

		wykonano / done	
<b>POWŁOKA OGNIOOCHRONNA</b> FIRE PROTECTION		<b>1 198,55</b>	[mb] [lm]
		29 [%]	

## TUNEL PRAWY

TUNNEL RIGHT

## POZOSTAŁO DO WYKONANIA

TO FINISH

		wg osi tunelu / by axis of the tunnel		wykonano / done	
<b>POWŁOKA OGNIOOCHRONNA</b> FIRE PROTECTION	start km	<b>721 844,16</b>		<b>943,74</b>	[mb] [lm]
	end km	<b>722 847,90</b>		46 [%]	

<b>POWŁOKA OGNIOOCHRONNA</b> FIRE PROTECTION	<b>960,71</b>	[mb] [lm]
---	---------------	--------------

\*\* NIE MA JESZCZE WYKONANEJ POWŁOKI NA ODCINKU / there is no fire protection yet  
od km 722 007,85 - 722 019,85 (12 mb), 722 179,85 - 722 191,85 (12 mb), 722 351,85 - 722 363,85 (12 mb), 722 523,85 - 722 535,85 (12 mb),  
722 695,85 - 722 707,85 (12 mb)

		wg osi tunelu / by axis of the tunnel		wykonano / done	
<b>POWŁOKA OGNIOOCHRONNA</b> FIRE PROTECTION	start km	<b>722 902,90</b>		<b>150,50</b>	[mb] [lm]
	end km	<b>723 077,40</b>		7 [%]	

\*\* NIE MA JESZCZE WYKONANEJ POWŁOKI NA ODCINKU / there is no fire protection yet  
od km 723 015,40 - 723 027,40 (12 mb), 723 041,40 - 723 053,40 (12 mb)  
722 695,85 - 722 707,85 (12 mb)
