

PROGRES DLA POWŁOKI OGNIOOCHRONNEJ

PROGRESS FOR FIRE PROTECTION

Progres na dzień:

30.01.2022

Progress for day:

TUNEL LEWY

TUNNEL LEFT

POWŁOKA OGNIOOCHRONNA	ŁĄCZNIE	949,06 [mb]
FIRE PROTECTION	TOTAL	[lm]
		46 [%]

WYKONANE ODCINKI / sections done

(km) wg osi tunelu / by axis of the tunnel

wykonano / done

721 818,46 - 722 077,77	259,31 [mb]
[lm]	[lm]
722 371,76 - 722 482,76	111,00 [mb]
[lm]	[lm]
722 508,76 - 722 532,76	24,00 [mb]
[lm]	[lm]
722 618,76 - 722 999,47	380,71 [mb]
[lm]	[lm]
723 186,47 - 723 321,47	135,00 [mb]
[lm]	[lm]
723 407,47 - 723 446,51	39,04 [mb]
[lm]	[lm]

POZOSTAŁO DO WYKONANIA


TO FINISH

POWŁOKA OGNIOOCHRONNA	1 067,16 [mb]
FIRE PROTECTION	[lm]
	43,24 [mb]
	[lm]
RAZEM	1 110,40 [mb]
TOTAL	[lm]

TUNEL LEWY

OBIEKT ST1

PORTAL PÓŁNOCNY / NORTH
2
1

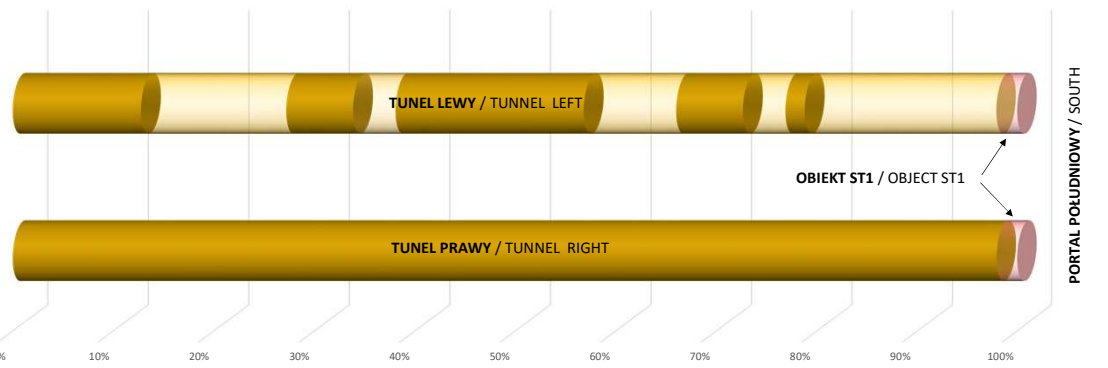

TUNEL LEWY I PRAWY

oraz OBIEKT ST1

TUNNEL LEFT AND RIGHT and OBJ. ST1

POWŁOKA OGNIOOCHRONNA	2 960,78 [mb]
FIRE PROTECTION	[lm]
	72 [%]

TUNEL PRAWY

TUNNEL RIGHT

POWŁOKA OGNIOOCHRONNA	start	721 844,16	2 011,72 [mb]
	end	723 855,88	[lm]
FIRE PROTECTION			98 [%]

POZOSTAŁO DO WYKONANIA

TO FINISH

POWŁOKA OGNIOOCHRONNA	0,00 [mb]
FIRE PROTECTION	[lm]
	43,24 [mb]
	[lm]
RAZEM	43,24 [mb]
TOTAL	[lm]

TUNEL PRAWY

OBIEKT ST1

OBIEKT ST1

POWŁOKA OGNIOOCHRONNA	start	723 855,88	0,00 [mb]
	end	723 899,12	[lm]
FIRE PROTECTION			0 [%]
