

PROGRES DLA POWŁOKI OGNIIOCHRONNEJ

PROGRESS FOR FIRE PROTECTION

Progres na dzień:

Progress for day:

06.02.2022

TUNEL LEWY

TUNNEL LEFT

POWŁOKA OGNIIOCHRONNA	ŁĄCZNIE	1 099,06 [mb] [lm]
FIRE PROTECTION	TOTAL	53 [%]

WYKONANE ODCINKI / sections done

[km] wg osi tunelu / by axis of the tunnel		wykonano / done
721 818,46	- 722 077,77	259,31 [mb] [lm]
722 371,76	- 722 532,76	161,00 [mb] [lm]
722 618,76	- 723 025,47	406,71 [mb] [lm]
723 186,47	- 723 359,47	173,00 [mb] [lm]
723 407,47	- 723 506,51	99,04 [mb] [lm]
		[mb] [lm]


POZOSTAŁO DO WYKONANIA

TO FINISH

POWŁOKA OGNIIOCHRONNA	917,16 [mb] [lm]
FIRE PROTECTION	43,24 [mb] [lm]
RAZEM	960,40 [mb] [lm]
TOTAL	

TUNEL LEWY

OBIEKT ST1

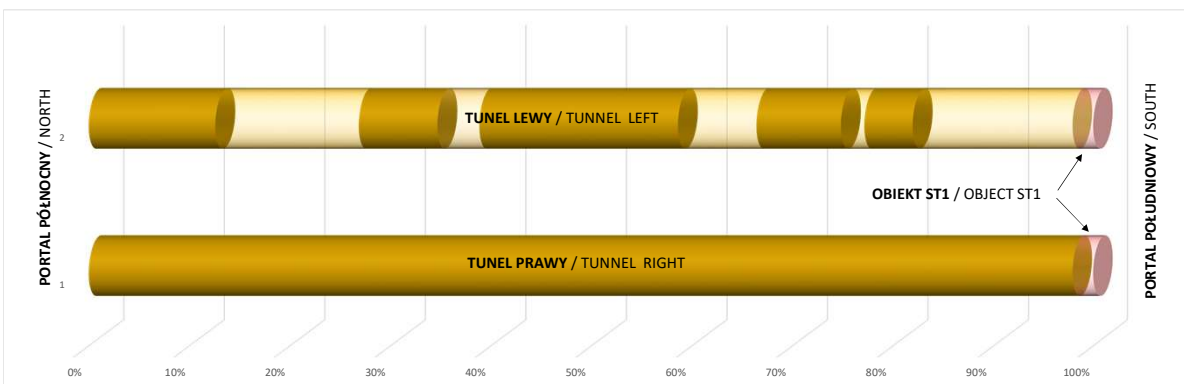

TUNEL LEWY I PRAWY

oraz OBIEKT ST1

TUNNEL LEFT AND RIGHT and OBJ. ST1

POWŁOKA OGNIIOCHRONNA

FIRE PROTECTION

wykonano / done

3 110,78 [mb]
[lm]

76 [%]

TUNEL PRAWY

TUNNEL RIGHT

POWŁOKA OGNIIOCHRONNA	start	721 844,16	2 011,72	[mb] [lm]
	end	723 855,88		98 [%]
FIRE PROTECTION				

POZOSTAŁO DO WYKONANIA

TO FINISH

POWŁOKA OGNIIOCHRONNA	0,00 [mb] [lm]
FIRE PROTECTION	43,24 [mb] [lm]
RAZEM	43,24 [mb] [lm]
TOTAL	

TUNEL PRAWY

OBIEKT ST1

OBIEKT ST1

POWŁOKA OGNIIOCHRONNA	start	723 855,88	0,00	[mb] [lm]
	end	723 899,12		0 [%]
FIRE PROTECTION				
