

PROGRES DLA POWŁOKI OGNIIOCHRONNEJ

PROGRESS FOR FIRE PROTECTION

Progres na dzień:

13.02.2022

Progress for day:

TUNEL LEWY

TUNNEL LEFT

POWŁOKA OGNIIOCHRONNA	ŁĄCZNIE	1 296,06 [mb]
FIRE PROTECTION	TOTAL	[lm]
		63 [%]

WYKONANE ODCINKI / sections done

[km] wg osi tunelu / by axis of the tunnel		wykonano / done
721 818,46	- 722 113,77	295,31 [mb]
722 371,76	- 722 594,76	223,00 [mb]
722 618,76	- 723 049,47	430,71 [mb]
723 186,47	- 723 383,47	197,00 [mb]
723 407,47	- 723 557,51	150,04 [mb]
-	-	[mb]


POZOSTAŁO DO WYKONANIA

TO FINISH

POWŁOKA OGNIIOCHRONNA	720,16 [mb]
FIRE PROTECTION	[lm]
	43,24 [mb]
	[lm]
RAZEM	763,40 [mb]
TOTAL	[lm]

TUNEL LEWY

OBIEKT ST1

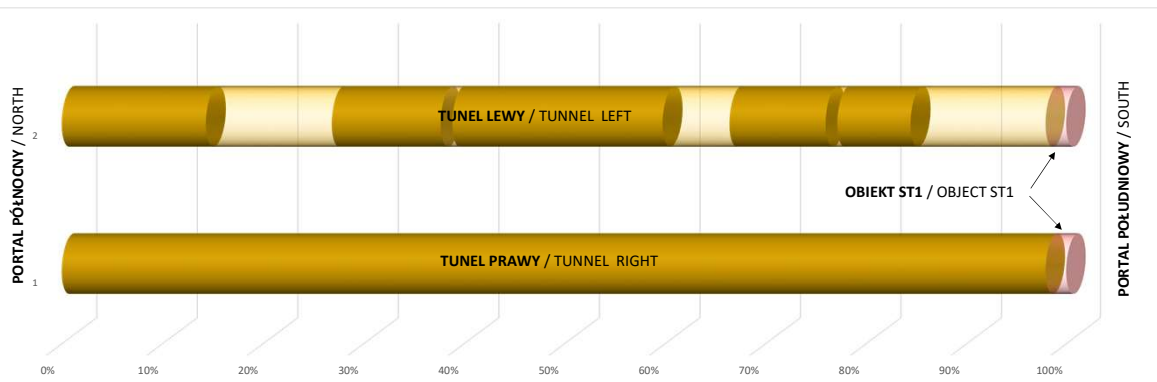

TUNEL LEWY I PRAWY

oraz OBIEKT ST1

TUNNEL LEFT AND RIGHT and OBJ. ST1

POWŁOKA OGNIIOCHRONNA

wykonano / done

3 307,78 [mb]

FIRE PROTECTION

80 [%]

TUNEL PRAWY

TUNNEL RIGHT

POWŁOKA OGNIIOCHRONNA	wg osi tunelu / by axis of the tunnel		wykonano / done
	start km	721 844,16	2 011,72 [mb]
	end km	723 855,88	[lm]
FIRE PROTECTION			98 [%]

POZOSTAŁO DO WYKONANIA

TO FINISH

POWŁOKA OGNIIOCHRONNA	0,00 [mb]
FIRE PROTECTION	[lm]
	43,24 [mb]
	[lm]
RAZEM	43,24 [mb]
TOTAL	[lm]

TUNEL PRAWY

OBIEKT ST1

OBIEKT ST1

POWŁOKA OGNIIOCHRONNA	wg osi tunelu / by axis of the tunnel		wykonano / done
	start km	723 855,88	0,00 [mb]
	end km	723 899,12	[lm]
FIRE PROTECTION			0 [%]
