

PROGRES DLA POWŁOKI OGNIIOCHRONNEJ

PROGRESS FOR FIRE PROTECTION

Progres na dzień:

27.02.2022

Progress for day:

TUNEL LEWY

TUNNEL LEFT

POWŁOKA OGNIIOCHRONNA

FIRE PROTECTION

ŁĄCZNIE

TOTAL

1 564,06 [mb]

[lm]

76 [%]

WYKONANE ODCINKI / sections done

[km] wg osi tunelu / by axis of the tunnel

wykonano / done

721 818,46	-	722 144,77	326,31	[mb]
				[lm]

722 316,76	-	723 073,47	756,71	[mb]
				[lm]

723 186,47	-	723 619,51	433,04	[mb]
				[lm]

723 619,51	-	723 667,51	48,00	[mb]
				[lm]

POZOSTAŁO DO WYKONANIA

TO FINISH

POWŁOKA OGNIIOCHRONNA

FIRE PROTECTION

452,16 [mb]

[lm]

43,24 [mb]

[lm]

RAZEM


TOTAL

495,40 [mb]

[lm]

TUNEL LEWY

OBIEKT ST1

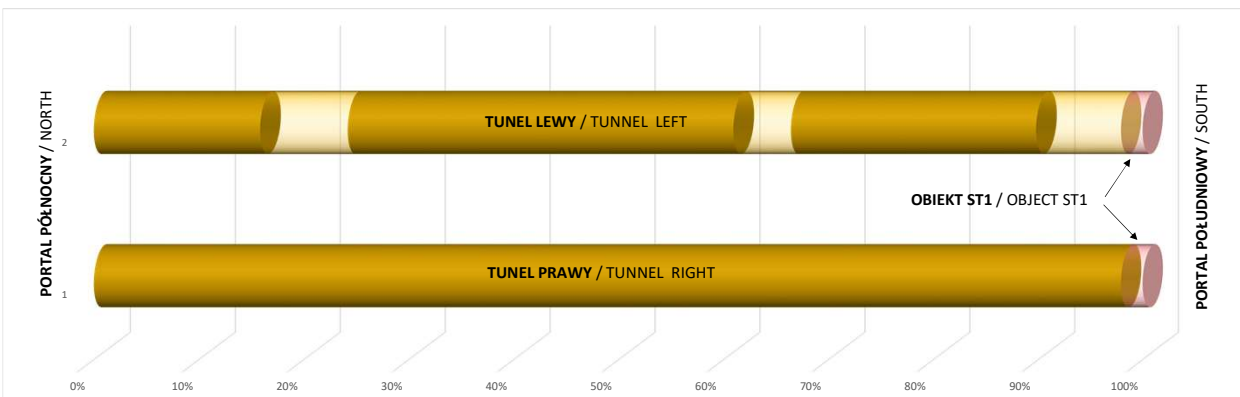

TUNEL LEWY I PRAWY

oraz OBIEKT ST1

TUNNEL LEFT AND RIGHT and OBJ. ST1

wykonano / done

POWŁOKA OGNIIOCHRONNA

FIRE PROTECTION

3 575,78 [mb]

[lm]

87 [%]

TUNEL PRAWY

TUNNEL RIGHT

POWŁOKA OGNIIOCHRONNA

FIRE PROTECTION

wg osi tunelu / by axis of the tunnel

wykonano / done

start

721 844,16

end

723 855,88

2 011,72 [mb]

[lm]

98 [%]

POZOSTAŁO DO WYKONANIA

TO FINISH

POWŁOKA OGNIIOCHRONNA

FIRE PROTECTION

0,00 [mb]

[lm]

43,24 [mb]

[lm]

RAZEM

TOTAL

43,24 [mb]

[lm]

TUNEL PRAWY

OBIEKT ST1

OBIEKT ST1

POWŁOKA OGNIIOCHRONNA

FIRE PROTECTION

wg osi tunelu / by axis of the tunnel

wykonano / done

start

723 855,88

end

723 899,12

0,00 [mb]

[lm]

0 [%]
