

PROGRES DLA POWŁOKI OGNIIOCHRONNEJ

PROGRESS FOR FIRE PROTECTION

Progres na dzień:

Progress for day:

24.10.2021

TUNEL LEWY


TUNNEL LEFT

POZOSTAŁO DO WYKONANIA

TO FINISH

		wg osi tunelu / by axis of the tunnel		wykonano / done	
POWŁOKA OGNIIOCHRONNA FIRE PROTECTION	start km	721 818,46	48,72 [mb] [lm]	2	[%]
	end km	721 867,18			

POWŁOKA OGNIIOCHRONNA FIRE PROTECTION	2 010,74 [mb] [lm]
------------------------------------------	-----------------------

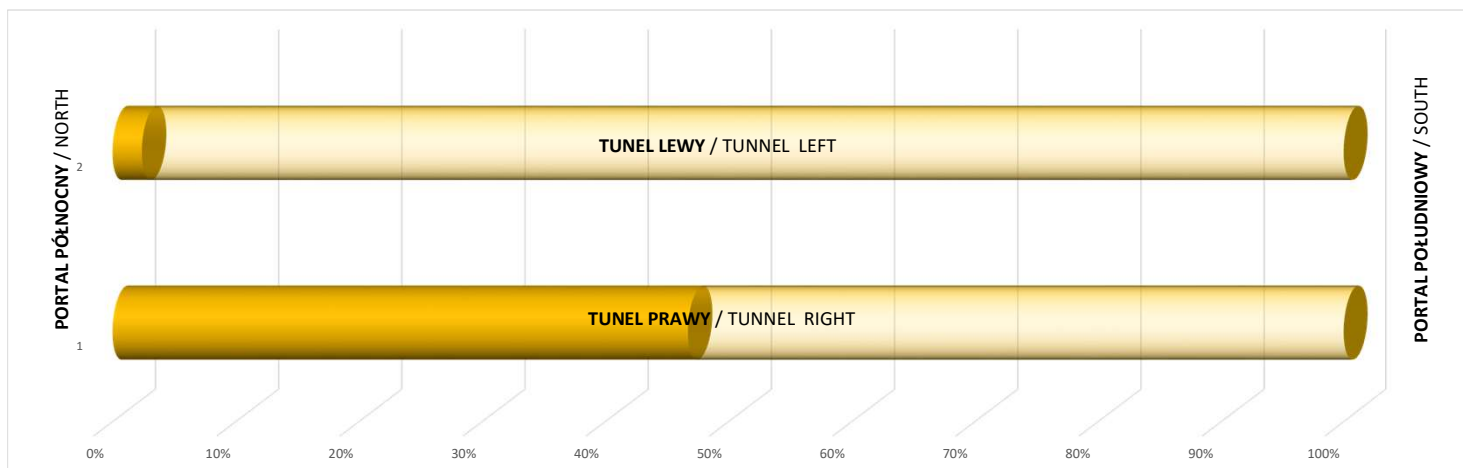

TUNEL LEWY I PRAWY

TUNNEL LEFT AND RIGHT

		wykonano / done	
POWŁOKA OGNIIOCHRONNA FIRE PROTECTION		974,41 [mb] [lm]	24
		[%]	

TUNEL PRAWY

TUNNEL RIGHT

POZOSTAŁO DO WYKONANIA

TO FINISH

		wg osi tunelu / by axis of the tunnel		wykonano / done	
POWŁOKA OGNIIOCHRONNA FIRE PROTECTION	start km	721 844,16	925,69 [mb] [lm]	45	[%]
	end km	722 829,85			

POWŁOKA OGNIIOCHRONNA FIRE PROTECTION	1 129,27 [mb] [lm]
------------------------------------------	-----------------------

** NIE MA JESZCZE WYKONANEJ POWŁOKI NA ODCINKU / there is no fire protection yet
od km 722 007,85 - 722 019,85 (12 mb), 722 179,85 - 722 191,85 (12 mb), 722 351,85 - 722 363,85 (12 mb), 722 523,85 - 722 535,85 (12 mb),
722 695,85 - 722 707,85 (12 mb)
