

PROGRES DLA POWŁOKI OGNIIOCHRONNEJ

PROGRESS FOR FIRE PROTECTION

Progres na dzień:

Progress for day:

19.12.2021

TUNEL LEWY

TUNNEL LEFT

| | | wg osi tunelu / by axis of the tunnel | | wykonano / done | |
|--|----------|---------------------------------------|---------------------|-----------------|--|
| POWŁOKA OGNIIOCHRONNA FIRE PROTECTION | start km | 721 818,46 | 196,31 [mb] [lm] | 10 [%] | |
| | end km | 722 014,77 | | | |

| | | wg osi tunelu / by axis of the tunnel | | wykonano / done | |
|--|----------|---------------------------------------|--------------------|-----------------|--|
| POWŁOKA OGNIIOCHRONNA FIRE PROTECTION | start km | 722 618,76 | 86,00 [mb] [lm] | 4 [%] | |
| | end km | 722 704,76 | | | |

| | | wg osi tunelu / by axis of the tunnel | | wykonano / done | |
|--|----------|---------------------------------------|--------------------|-----------------|--|
| POWŁOKA OGNIIOCHRONNA FIRE PROTECTION | start km | 723 186,47 | 48,00 [mb] [lm] | 2 [%] | |
| | end km | 723 234,47 | | | |


POZOSTAŁO DO WYKONANIA

TO FINISH

| | |
|--|-------------------------------|
| POWŁOKA OGNIIOCHRONNA FIRE PROTECTION | 1 685,91 [mb] [lm] |
| | 43,24 [mb] [lm] |
| RAZEM TOTAL | 1 729,15 [mb] [lm] |

TUNEL LEWY

OBIEKT ST1

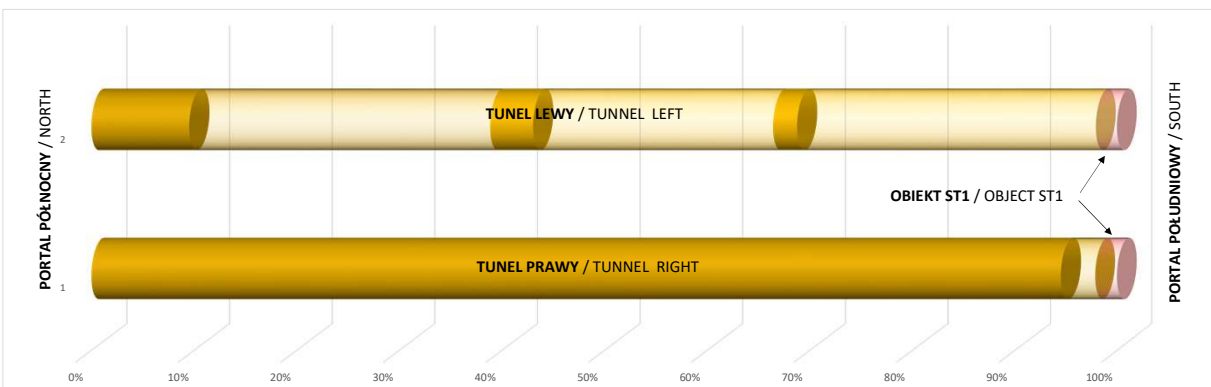

TUNEL LEWY I PRAWY

oraz OBIEKT ST1

TUNNEL LEFT AND RIGHT and OBJ. ST1

| | | wykonano / done | |
|--|-----------------------|-----------------|--|
| POWŁOKA OGNIIOCHRONNA FIRE PROTECTION | 2 214,72 [mb] [lm] | 54 [%] | |

TUNEL PRAWY

TUNNEL RIGHT

| | | wg osi tunelu / by axis of the tunnel | | wykonano / done | |
|--|----------|---------------------------------------|-----------------------|-----------------|--|
| POWŁOKA OGNIIOCHRONNA FIRE PROTECTION | start km | 721 844,16 | 1 884,41 [mb] [lm] | 92 [%] | |
| | end km | 723 788,57 | | | |

POZOSTAŁO DO WYKONANIA

TO FINISH

| | |
|--|-----------------------------|
| POWŁOKA OGNIIOCHRONNA FIRE PROTECTION | 127,31 [mb] [lm] |
| | 43,24 [mb] [lm] |
| RAZEM TOTAL | 170,55 [mb] [lm] |

TUNEL PRAWY

OBIEKT ST1

** NIE MA JESZCZE WYKONANEJ POWŁOKI NA ODCINKU / there is no fire protection yet
od km 722 351,85 - 722 363,85 (12mb; CP039), 722 695,85 - 722 707,85 (12 mb; CP071), 722 869,40 - 722 881,40 (12 mb;
CP087), 723 213,40 - 723 225,40 (12 mb; CP119), 723 557,43 - 723 569,43 (12mb; CP151)
